
CONSTRUCTION ORDER


- 1. FIRST FLOOR PLATFORMS LAID OUT, SECURED TOGETHER, AND LEVELED
- SHEATHING APPLIED
- FIRST FLOOR WALLS INSTALLED
- ONE SIDE OF SHEATHING APPLIED
- 5. STAIRS INSTALLED
- 6. DOUBLE TOP PLATES ATTACHED
- 7. SECOND FLOOR PLATFORMS INSTALLED
- 8. SHEATHING APPLIED
- SECOND FLOOR WALLS INSTALLED
- 10. ONE SIDE OF SHEATHING APPLIED
- 11. ELECTRONICS WIRED
- 12. SHEATHING COMPLETED
- 13. ROOF PLATFORMS INSTALLED
- 14. DECORATIVE ELEMENTS ATTACHED

DECONSTRUCTION ORDER

- 15. DECORATIVE ELEMENTS REMOVED
- 16. ROOF PLATFORMS REMOVED
- 17. SECOND FLOOR SHEATHING REMOVED
- 18. WIRING REMOVED
- 19. SECOND FLOOR WALLS REMOVED
- 20. SECOND FLOOR PLATFORMS REMOVED
- 21. FIRST FLOOR SHEATHING REMOVED
- 22. FIRST FLOOR WALLS REMOVED
- 23. FIRST FLOOR PLATFORMS REMOVED

ALL REMOVED WOOD TO BE DELIVERED BACK TO THE BOOTH GARAGE, DISASSEMBLED, AND SAVED FOR REUSE. WOOD WE ARE NOT WILLING TO REUSE WILL BE DONATED TO CONSTRUCTION JUNCTION, PROJECT RE, OR FREEDOM BY DESIGN DEPENDING ON SIZE.



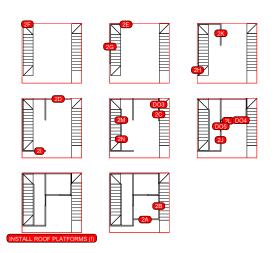

ASSEMBLY AND DISASSEMBLY

REFER TO PAGES 38 AND 96 FOR FIRST AND SECOND FLOOR ASSEMBLY ORDERS RESPECTIVELY

SIGEP BOOTH 2019 PAGE 22
